

Assignment 2

Total Points: 150

Submission Deadline: 27th March, 2026 at 11:59 PM

Late Submissions

Late submissions will lead to a deduction from the obtained marks. The following rules will apply:

- 0–10 mins late: 10% deduction
 - 11–30 mins late: 20% deduction
 - 31–60 mins late: 30% deduction
 - Beyond 1st hour (same day): 40% deduction
 - Up to 2 days late: 50% deduction (max)
 - After 2 days: Zero marks
-

In Assignment 1, a business case was prepared and a project was selected for each section. The project has been decomposed into multiple modules (sub-projects) during one of the lectures. Each group is responsible for managing and developing one module, while one group is designated as the Integration Group.

The Integration Group is responsible for both:

- Project Integration – integrating plans from all groups into an overall project plan
- Product Integration – ensuring that all modules integrate into a single working system

This assignment focuses on scope planning, schedule planning, and formal documentation. Students will begin producing structured project documents using the provided Project Management Plan template.


Pre-requisites

- Select a project integration group for your section / project.
- Pick one module with the consensus of all groups of your section. In case of a conflict, the integration group will have the final say. The integration group will not select any module.
- All groups, except the integration group, must select a group leader. The group leader is just a representative, not the 'owner' of your group. Every group member will be held accountable for any problems / failures.
- The integration group must decompose a module if the size of the module is large.
- Good selection of modules is very important for the success of your project. Work with each other to come up with any new module, if required.

Working Process for Assignment 2

All groups must follow the process below:

1. **Project Charter:** only one charter will be made and submitted for one section. All group leaders and the integration group must work together in drafting the charter. The group leaders should take into consideration the feedback or opinions of their group members.
The start date of the project is 12th March.
2. **Kickoff Meeting:** the meeting must be initiated and recorded by the integration group.
 - All groups and their group members must participate in a project kickoff meeting.
 - Scope boundaries, module responsibilities, and overall schedule strategy are discussed.
 - Deadlines for module deliverables are agreed upon.
 - Tentative future plan is decided.
3. **Planning Alignment:** Groups collaboratively agree on: the overall project scope, module boundaries, integration points, and high-level schedule and milestones.
4. **Module Planning:** Each group elaborates the scope and schedule for its assigned module.
5. **Integration:** Groups submit their planning outputs to the Integration Group. The Integration Group incorporates these plans into the overall project plan.
6. **Development:** all groups must work simultaneously on the software development. No separate instructions will be provided to start the development.

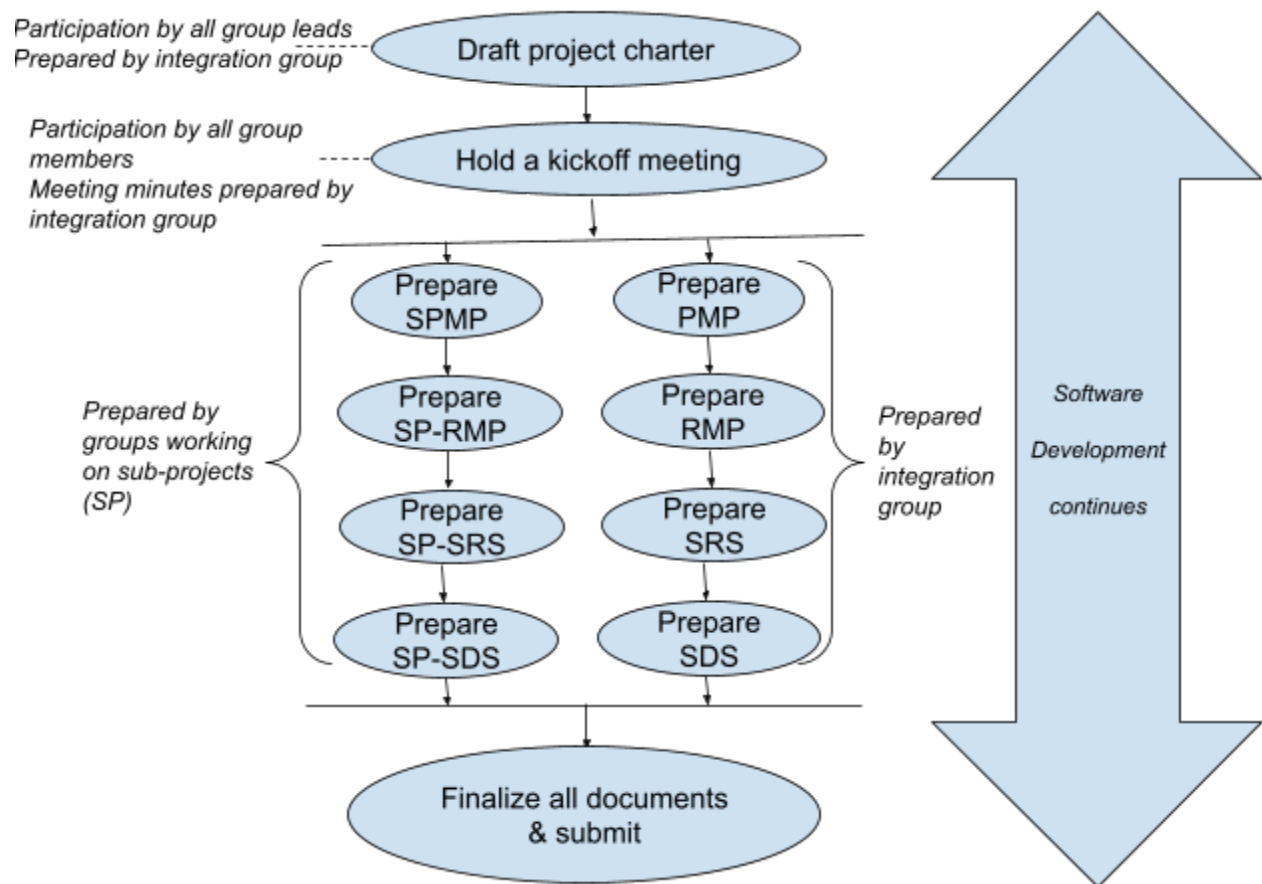

Project Deliverables

These deliverables focus on project planning and management.

1. Project Charter (One Submission per Section)

It is a joint effort of all the group leads and the integration group. Use the templates provided in the textbook.

Responsibility	Description
Team Leads	Collaboratively decide the project charter components.
Integration Group	Prepare the charter and get it signed by all the team leads.
Output	Project Charter

2. Kickoff Meeting

See the details and meeting minutes template in the textbook.

Responsibility	Description
All Group Members	Participate in the meeting and collaboratively decide scope, schedule, and other milestones.
Integration Group	Prepare meeting agenda and record meeting minutes
Output	Kickoff meeting minutes document

The kickoff meeting should finalize overall scope boundaries, module responsibilities, integration expectations, schedule coordination, and assignment-2 execution plan.

3. Project Management Plan (PMP) and Sub-Project Management Plans (SPMP)

Each group must prepare a Project Management Plan using the provided template. This assignment focuses only on scope and schedule related sections. You must refer to the textbook for templates or contents of scope statement, WBS, stakeholder register and management strategy, gantt charts, network diagrams, scope management plan, schedule management plan, etc.

Required Sections

Every group must complete the following sections:

Section	Description
Executive Summary	Brief description of the project/sub-project
Project Scope	Must include major elements of a scope statement
Deliverables	Product and process deliverables of the project/sub-project
WBS	Work Breakdown Structure of the project/sub-project
Stakeholder Analysis	Stakeholders relevant to the project/sub-project
Schedule Baseline	Planned schedule for the project/sub-project
Milestone List	Major milestones and dates of project/sub-project
Project Scope Management Plan	How scope will be defined and controlled for project/sub-project
Project Staff List	Team members of project/sub-project and assigned tasks
Schedule Management Plan	How the schedule of project/sub-project will be created and tracked
Authorization Signatures	Team lead signatures

The Project Staff List must include task assignments for each team member. Tasks must be derived from the WBS work packages.

Responsibilities for PMP Preparation

1. **Module Groups:** Each module group must prepare a Project Management Plan for their sub-project (SPMP). The SPMPs will serve as inputs for the overall project plan. The SPMP must include:
 - Scope statement of the module
 - Sub-project and module deliverables
 - Sub-project and module WBS
 - Sub-project schedule baseline
 - Sub-project milestones
 - Sub-project stakeholders
 - Task assignments for team members
 - Any other required information
2. **Integration Group:** The Integration Group must prepare the Overall Project Management Plan (PMP). The Integration Group may reference other SPMPs rather than copying them. Their plan must:
 - Incorporate WBS elements from all sub-projects to create overall project WBS; the overall project WBS will also include activities that integration group is responsible for.

- Integrate sub-project schedules into one overall schedule baseline; the overall schedule baseline will also include activities that integration group is responsible for.
- Define project-level milestones
- Describe integration checkpoints
- Coordinate sub-project and module dependencies

4. Product Deliverables

These deliverables focus on requirements and design documentation.

4.1. Requirements Management Plan

The contents of the requirements management plan should be taken from the textbook.

Group Type	Responsibility
Module Groups	Create requirements management plan for their module (SP-RMP)
Integration Group	Create an overall requirements management plan (RMP) for the entire system. It may reference module plans instead of duplicating content

4.2. Software Requirements Specification

The contents and template of this document can be taken from this [source](#).

Group Type	Responsibility
Module Groups	Prepare SP-SRS for their module
Integration Group	Prepare system-level SRS referencing module SRS documents

4.3. Software Design Specification

The contents of this document can be taken from this [source](#).

Group Type	Responsibility
Module Groups	Prepare detailed design document (SP-SDS) for their module
Integration Group	Prepare overall system design (SDS) and refer to module designs rather than copying them

Responsibility Assignment Matrix

R = responsible group for success and failure of the deliverable (includes accountability, participation, and consultation)

P = performing group for preparing and submitting the deliverable

	Project charter	Kickoff meeting	PMP	SPMP	RMP	SP-RMP	SRS	SP-SRS	SDS	SP-SDS
Module Groups	R	R	R	R, P	R	R, P	R	R, P	R	R, P
Integration Groups	R, P	R, P	R, P	R	R, P	R	R, P	R	R, P	R

Important Notes

- All documentation must follow formal professional standards.
- Documents must clearly show traceability and consistency between scope, WBS, and schedule.
- Sub-project/module plans must align with the overall system scope and schedule decided in the kickoff meeting.
- Integration plans must reflect inputs from module groups.

Marks Distribution

- Project Charter: 10
- Kickoff Meeting and Meeting Minutes: 10
- PMP/SPMP: 50
- RMP/SRMP: 20
- SRS/SP-SRS: 30
- SDS/SP-SDS: 30
